




SCHEMATIC

Milne Point Unit
Well: MPU E-43
Last Completed: 9/14/2026
PTD: 226-079

Orig. KB Elev.: 67.6' / GL Elev.: 20.6'

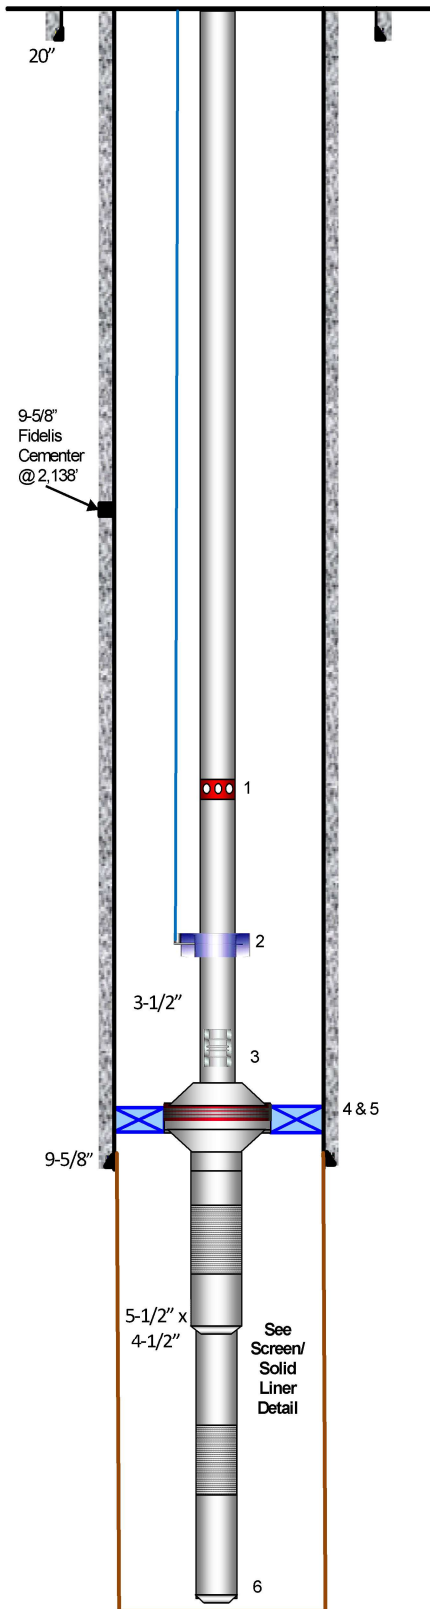

TREE & WELLHEAD

Tree	Cameron 3-1/8" 5M w/ 3-1/8" 5M Cameron Wing
Wellhead	FMC 11" 5K x sliplock bottom w/ (2) 2-1/16" 5K outs

OPEN HOLE / CEMENT DETAIL

42"	15 yds Concrete
12-1/4"	Stg 1 Lead – 1,077 sx / Tail – 422 sx Stg 2 Lead – 886 sx / Tail – 270 sx
8-1/2"	Cementless Screened Liner

CASING DETAIL

Size	Type	Wt/ Grade/ Conn	ID	Top	Btm	BPF
20"	Conductor	129.5# / X52 / Weld	N/A	Surface	154'	N/A
9-5/8"	Surface	47# / L-80 / TXP	8.681	Surface	2,142'	0.0732
9-5/8"	Surface	40# / L-80 / TXP	8.835	2,142'	8,821'	0.0758
5-1/2"	Liner	17# / L-80 / JFE Bear	4.892	8,645'	8,807'	0.0232
4-1/2"	Liner 250µ Screens	13.5# / L-80 / Hyd 625	3.920	8,807'	15,909'	0.0149

TUBING DETAIL

3-1/2"	Tubing	9.3# / L-80 / EUE 8rd	2.992	Surface	8,676'	0.0087
--------	--------	-----------------------	-------	---------	--------	--------

WELL INCLINATION DETAIL

KOP @ 248'
90° Hole Angle = @ 9,070'

JEWELRY DETAIL

No.	MD	Item	ID
1	8,072'	Sliding Sleeve	2.810"
2	8,125'	Gauge Mandrel Sage Rider	2.810"
3	8,178'	3.5" XN Nipple 2.813" Profile w/ 2.75" NoGo Nipple	2.750"
4	8,645'	SLZXP 7" x 9-5/8" LTP W/11.26" PBR (7.375" ID)	7.375"
5	8,668'	4.75" Seal Bore Extension	4.750"
6	15,909'	Shoe (Non-Ported Conventional Bull Nose)	

4-1/2" SCREENS LINER DETAIL

Size	Top (MD)	Top (TVD)	Btm (MD)	Btm (TVD)
4-1/2"	8,850'	4,287'	15,542'	4,413'

GENERAL WELL INFO

API: 50-029-23850-00-00
Completion Date: 9/14/2026

TD = 15,909' (MD) / TD = 4,441' (TVD)
PBD = 15,908' (MD) / PBD = 4,440' (TVD)
